

Lesson Five

Launch of software project

Effective Project Management: Traditional, Agile, Extreme

Ch08: How to Launch a TPM Project

***Presented by
Bowen DU***

Lesson **Five**: Launch of software project

Tools, Templates & Processes Used to Launch a Project

- Recruiting the Project Team
- Team Operating Rules
 - Problem Solving
 - Decision Making
 - Conflict Resolution
 - Consensus Building
 - Brainstorming
 - Team Meetings
- Scope change management process
- Communications management planning
- Work packages
- Resource assignment
- Finalize the project schedule

Lesson Five: Launch of software project

What Is a Project Team?

- A project team is a group of professionals committed to achieving common objectives, who work well together, and who relate directly and openly with one another to get things done.
- Project team membership
 - Co-Project manager – developer (chosen before Scoping)
 - Co-Project manager – client (chosen before Scoping)
 - Core team (chosen before Planning)
 - Developer team (chosen before Launching)
 - Client team (chosen before Launching)
 - Contracted team (chosen after Launching)



Lesson **Five**: Launch of software project

Characteristics of the Core Team

- Commitment
- Shared responsibility
- Flexibility
- Task-oriented
- Ability to work within schedules and constraints
- Willingness for trust and mutual support
- Team-oriented
- Open-minded
- Ability to work across structure and authorities
- Ability to use project management tools

Lesson **Five**: Launch of software project

Client Team Members

- Must understand their business unit processes.
- Must be able to make decisions and commitments for their business unit.

Lesson **Five**: Launch of software project

Contract Team Members - Implications

- Little variance in times they are available.
- Know how their tasks relate to the project.
- Commitment can be a problem.
- Quality of work may be poor.
- May require more supervision than core team.

Lesson **Five**: Launch of software project

Balancing a Team

- Developing a team deployment strategy.
- Developing a team development plan.



Lesson **Five**: Launch of software project


Where Project Teams Can Improve

- Work methods and procedures.
- Knows appropriate technology.
- Associate attraction and retention.
- Staffing flexibility.
- Service and product quality use.
- Rate of output.
- Decision making.
- Reduced staff support level.
- Reduced supervision.

Lesson **Five**: Launch of software project

Team Member Responsibilities

- Open communication
- Good listening skills
- Shared goals
- Positive outlook
- Creativity
- Respect for others
- Growth and learning

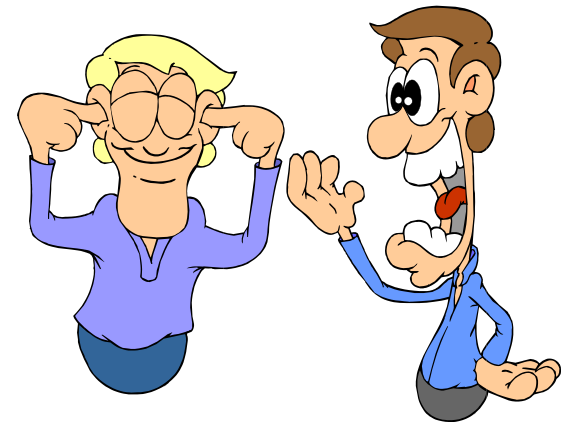

Lesson **Five**: Launch of software project

The Working Session Project Manager-led Agenda

- Introduce the project team members to each other.
- Write the Project Definition Statement (PDS).
- Establish team operating rules
 - Problem solving
 - Decision making
 - Conflict resolution
 - Consensus building
 - Brainstorming
 - Team meetings
- Review the project plan.
- Finalize the project schedule.
- Write work packages.

Lesson **Five**: Launch of software project

Project Definition Statement – Contents

- Expands the POS
 - Project objectives.
 - Assumptions, risks, and obstacles.

Lesson **Five**: Launch of software project

Project Definition Statement – Purpose

- As a basis for continued project planning.
- To clarify the project for the project team.
- As a reference that keeps the team focused in the right direction.
- As an orientation for new team members.
- As a method for discovery by the team.

Lesson **Five**: Launch of software project

Project Charter – Template

Project Name or Identification

Project Stakeholders

- Names
- Titles or roles
- Phone numbers
- E-mail addresses

Project Description

- Background
- Description of the challenge or opportunity
- Overview of the desired impact

Measurable Organizational Value (MOV)

- Statement or table format

Project Scope

- What will be included in the scope of this project
- What will be considered outside the scope of this project

Project Schedule Summary

- Project start date
- Project end date
- Timeline of project phases and milestones
- Project reviews and review dates

Project Budget Summary

- Total project budget
- Budget broken down by phase

Quality Issues

- Specific quality requirements

Resources Required

- People

- Technology
- Facilities
- Other
- Resources to be provided
 - Resource
 - Name of resource provider
 - Date to be provided

Assumptions and Risks

- Assumptions used to develop estimates
- Key risks, probability of occurrence, and impact
- Constraints
- Dependencies on other projects or areas within or outside the organization
- Assessment project's impact on the organization
- Outstanding issues

Project Administration

- Communications plan
- Scope management plan
- Quality management plan
- Change management plan
- Human resources plan
- Implementation and project closure plan

Acceptance and Approval

- Names, signatures, and dates for approval

References

Terminology or Glossary

Appendices (as required)

Lesson **Five**: Launch of software project

Establishing Team Operating Rules

- Problem solving
- Decision making
- Conflict resolution
- Consensus building
- Brainstorming
- Team meetings

Lesson **Five**: Launch of software project

Five Steps to Solving a Problem

1. Define the problem & the owner
2. Gather relevant data and analyze causes
3. Generate ideas
4. Evaluate and prioritize ideas
5. Develop an action plan



Lesson **Five**: Launch of software project

Team Meetings

- What is your purpose?
- How often?
- How long?
- Who should attend?
- Do we need an agenda?
- Are there minutes? Who takes them? Who gets them?

Lesson **Five**: Launch of software project

Guidelines for Managing Meetings

- Before the Meeting
 - Is the meeting necessary?
 - Determine the purpose of the meeting
 - Set the ground rules for the discussion
 - Determine who really needs to be present and only invite those people
 - Make notes and rehearse your presentation
 - Start and end the meeting on time

Lesson **Five**: Launch of software project

Guidelines for Managing Meetings

- During the Meeting
 - Specify a time limit and stick to it
 - Identifying the specific objectives
 - Gather input from the participants
 - Keep things moving
 - Use visual aids
 - Periodically summarize the results of the discussion in terms of consensus achieved or disagreements still in progress
 - Assign action items to team members



Lesson **Five**: Launch of software project

Guidelines for Managing Meetings

➤ After the Meeting

- Time, place, and instructions for the next meeting
- Time and place of the meeting and list of attendees with their project role
- Agenda items discussed
- Decisions reached or held for further studies
- Action items and persons responsible for follow up and reporting back to the team at the next meeting

Lesson **Five**: Launch of software project

Project Meetings

- Daily status meetings
- Problem resolution meetings
- Project review meetings
 - Frequency
 - Length
 - Purpose
 - Team room

Lesson **Five**: Launch of software project

Daily Status Meetings

- 15 minutes
- Everyone stands
- Only reporting on tasks open for work and not yet done
- Status
 - I'm on plan
 - I am **xx** hours behind schedule but have a plan to be caught up by this time tomorrow
 - I am **xx** hours behind plan and need help
 - I am **xx** hours ahead of plan and available to help

Lesson **Five**: Launch of software project

Problem Resolution Meeting Agenda

- Only attended by those involved in the problem
- Who owns the problem?
- What is the resolution?
- When will it be completed?


Lesson **Five**: Launch of software project

Project Review Meetings

- Held at project milestone events
- Project review panel
- Formal presentation of project performance to date

Lesson **Five**: Launch of software project

Typical Scope Change Management Process

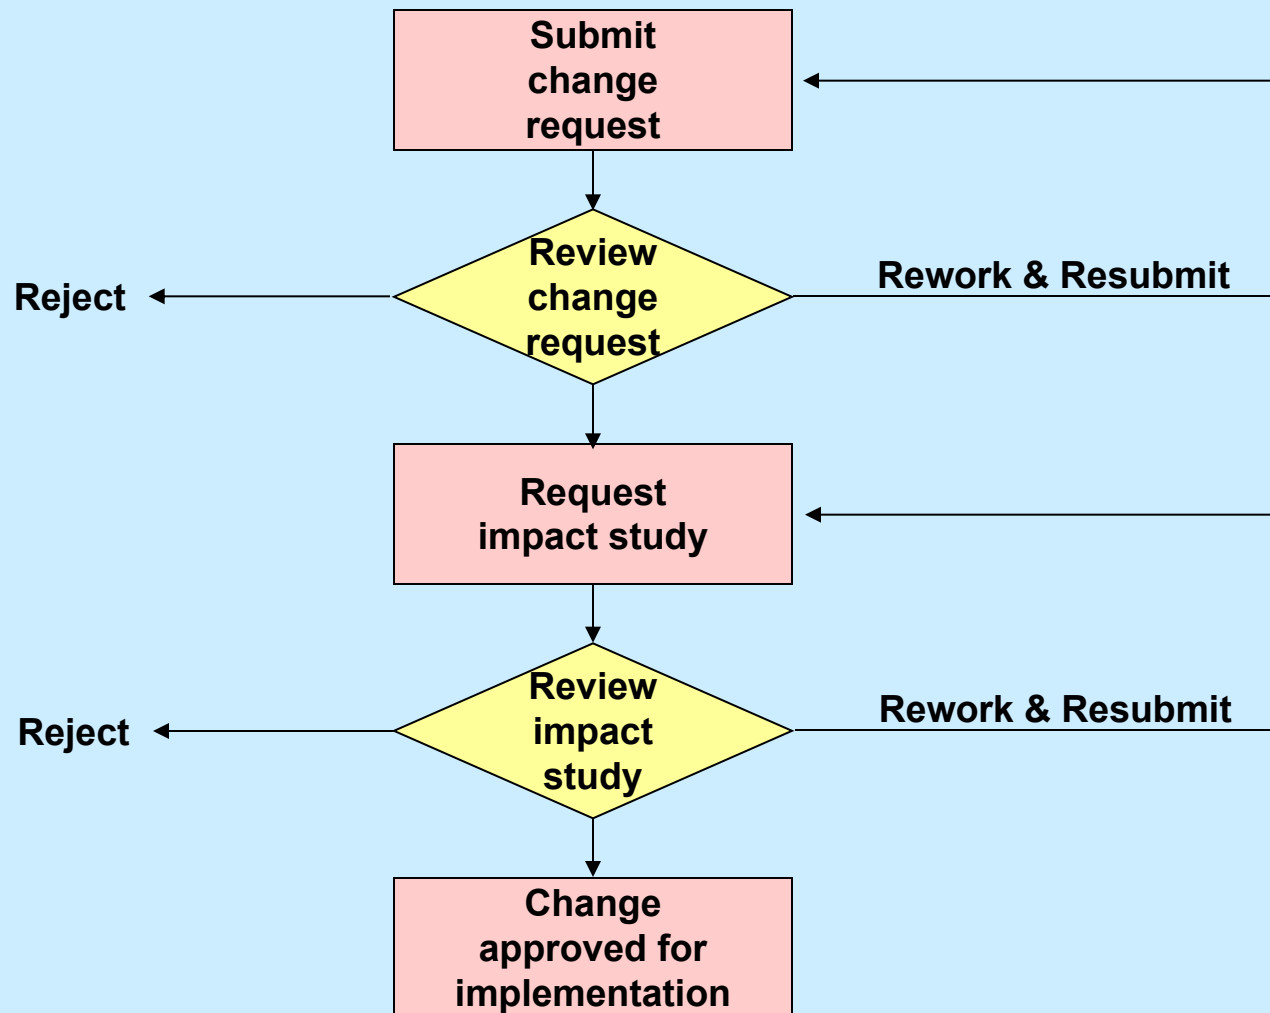

Lesson **Five**: Launch of software project

Project Impact Statement - Contents

- What is the expected benefit of the change?
- How would the change affect the project's cost?
- How would the change affect the project's schedule?
- How would the change affect the software's quality?
- How would the change affect the project's resource allocation?
- Can the change be deferred to a later stage of the project or a later version of the software?
- Is the project at a point when making the change would risk destabilizing(破坏) the software?

Lesson **Five**: Launch of software project

Scope Change Request Form

Project Name

Change Requested By

Date Change Requested

Description of Change

Business Justification

Action

Approved By

Date

Lesson **Five**: Launch of software project

Tips to Help the Client Understand Scope Change

- Business needs change or are discovered during the project
- Scope change requests are expected
- Project team will analyze the request's impact on the project plan
- Project impact statement will define alternatives for accommodating the request
- Client will choose the alternative to be followed
- Project manager will adjust project plan accordingly and inform the client

Lesson **Five**: Launch of software project

Management Reserve

- A percentage (5-10%) of the project duration is set aside as a time contingency for processing and incorporating scope change requests.
- Utilizing a Scope Bank to store prioritized functions and features not yet integrated into the solution will help manage Management Reserve.

Lesson **Five**: Launch of software project

Scope Bank

- Set up a scope request bank account with an initial deposit of time (5-10 percent of total project work time) to be used to process cope changes and adjust the schedule.
- Utilize the Scope Bank to store prioritized change requests not yet integrated into the solution.
- Change requests can be handled at the end of a project cycle or as needed.

Lesson **Five**: Launch of software project


Managing Team Communications

Establishing a communications model including:

- Timing
- Content
- Choosing Effective Channels

Lesson **Five**: Launch of software project

Communications Management – The Process

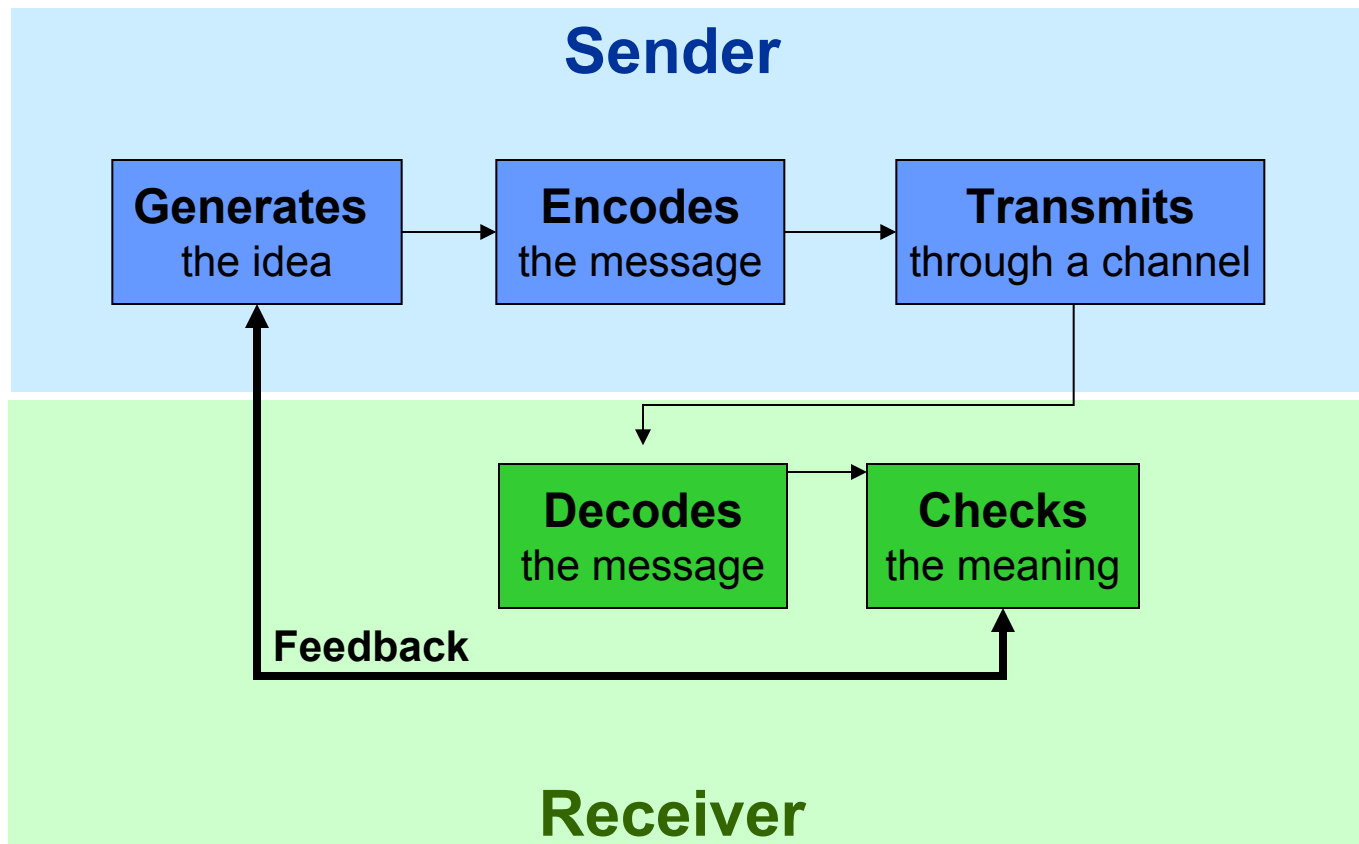


Lesson **Five**: Launch of software project

Communications Management – Types

- One-to-one
 - Conversations (in person and on the phone)
 - Meetings
- Electronic
 - Email messages
 - Web sites
 - Databases
- Written
 - Memos
 - Letters
 - Documents
 - Reports

Lesson **Five**: Launch of software project

Communications Management – Interfaces

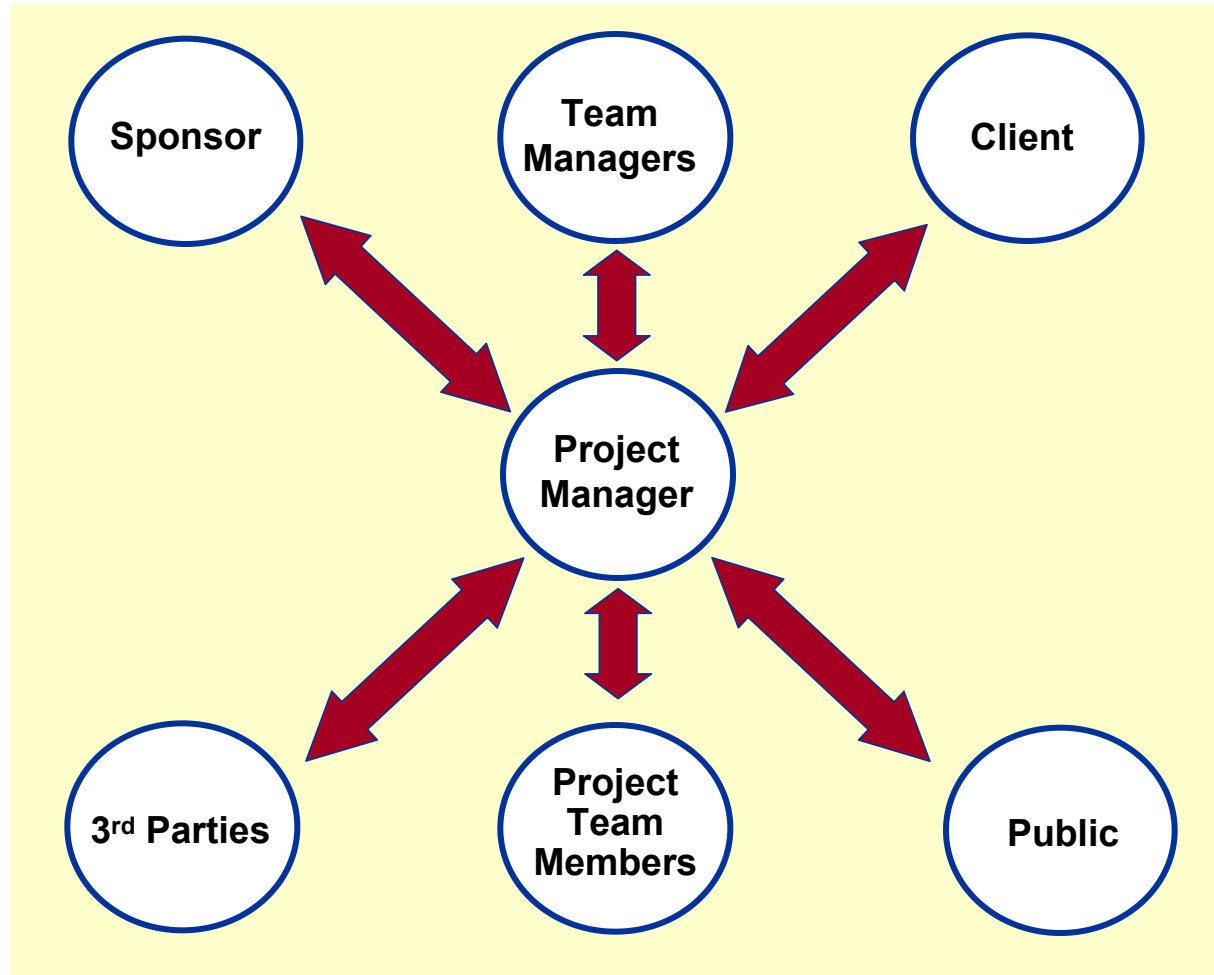

Lesson **Five**: Launch of software project

Delegation: RASCI Matrix

T A S K S		Jack	Bob	Cheryl
	Confirm customer approval of scope	R	S	
	Choose project team	R	I	A
	Plan project	S	R	
	Define Budget	C	R	I
	Plan Kick-Off Meeting	I		R

R= Responsible, accountable for successful completion

A= Needs to Approve decisions

S= Will provide Support for the “R”

C= Available to Coach and Consult

I= Needs to be kept informed of status


Lesson **Five**: Launch of software project

Expanded Variation of the RASCI Matrix

Tasks	Task Lead	Start Date	End Date	Est. End	Pred.	Succ.	CP?	Comments
A	Jack	7/1/08	7/3/08	7/2/08	Start	B	Y	
B	Bob	7/5/08	XXXX	7/13/08	A	D	Y	
C	Cheryl	7/5/08	7/10/08	7/13/08	A	D	N	
D	Harry	7/14/04 8	7/16/08	7/14/08	B C	End	Y	

Lesson **Five**: Launch of software project

Assigning Resources

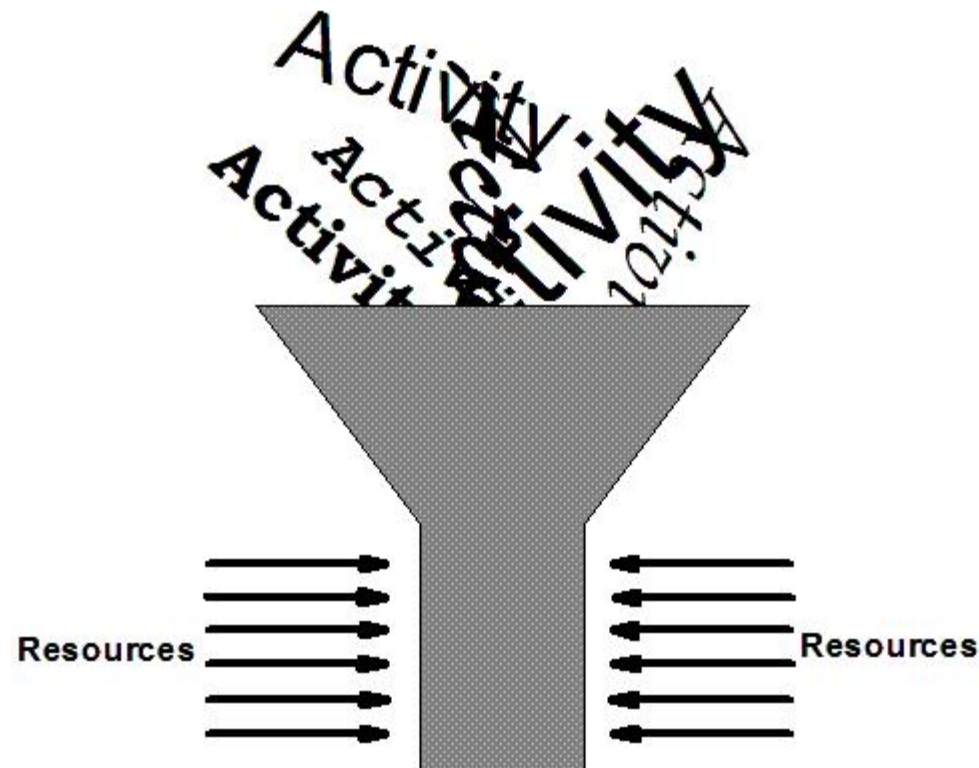

Lesson **Five**: Launch of software project

Resource-Leveling Strategies

- Utilizing available slack
- Shifting the project finish date
- Smoothing


Lesson **Five**: Launch of software project

Alternative Methods of Scheduling Tasks

- Further decomposition of tasks
- Stretching tasks
- Assigning substitute resources

Lesson **Five**: Launch of software project

Launch the Project – Finalize Resources & Schedule

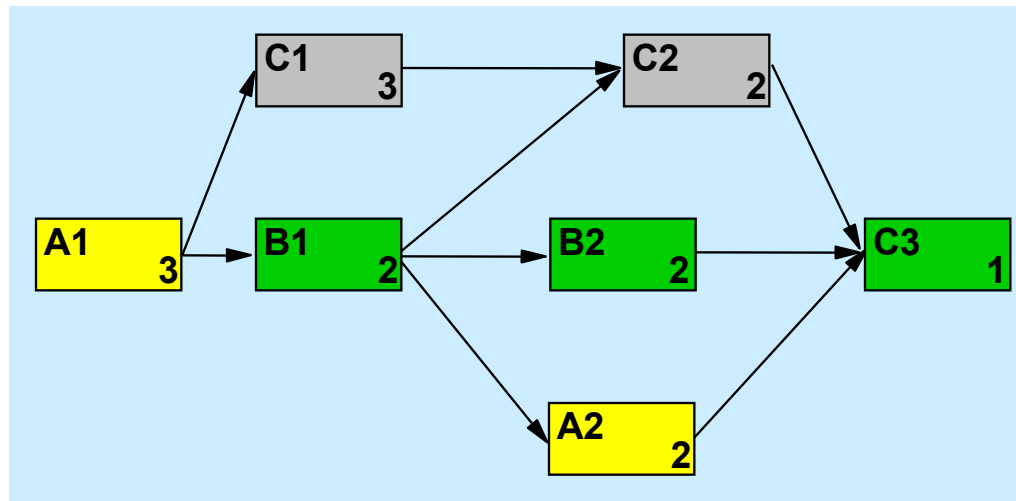

	M	T	W	R	F	S	S	M	T	W	R	F	S	S
Duffy	a1	a1	a1	/				a2	a2					
Ernie				b1	b1			b2	b2	/				
Fran			/	c1	c1			c1	c2	c2	/	c2	c3	/

Lesson **Five**: Launch of software project

Launch the Project – Work Packages

- A Work Package is a brief description at the subtask level that describes how a task will be completed. It is a primitive(初始) project plan.

- Work Packages should be written for:
 - Critical path tasks
 - High-risk tasks
 - Tasks requiring scarce resources
 - Tasks with large duration variances

Lesson **Five**: Launch of software project

Launch the Project – Work Package Assignment Sheet

WORK PACKAGE ASSIGNMENT SHEET		Project Name		Project No.		Project Manager	
Work Package		Schedule		Work Package Manager		Contact Information	
Number	Name	Early Start	Late Finish				
A	DESIGN	03/01/08	04/01/08	ANNA LYST			
B	PROD.EVAL	04/02/08	07/02/08	HY ROWLER			
C1	PLACE.LOCATE.PT1	04/02/08	03/04/09	SY YONARA			
C2	PLACE.LOCATE.PT2	07/03/08	03/04/09	HY ROWLER			
D	PROD.FCAST	07/03/08	03/04/09	SY YONARA			
E	PROD.DELETE	03/05/09	06/02/09	HY ROWLER			
F	PROMO.REGION	03/05/09	07/06/09	TERRI TORY			
H	PRICE	08/04/09	02/05/10	HY ROWLER			
I	PLACE.DESIGN	06/05/09	08/03/10	HY ROWLER			
J	PROMO.SALES.LEAD	07/07/09	11/05/09	TERRI TORY			
G	PROMO.MEDIA	07/07/09	02/05/10	SY YONARA			
K	PROMO.SALES.RPT	10/07/09	02/05/10	TERRI TORY			
L	SYSTEM.TEST	02/08/10	05/10/10	ANNA LYST			
M	SYSTEM.ACCEPT	05/10/10	06/10/10	ANNA LYST			
Prepared by		Date		Approved by		Date	
						Sheet 1 of 1	

Lesson **Five**: Launch of software project

Launch the Project – Work Package Description Form

WORK PACKAGE DESCRIPTION			Project Name		Project No.		Project Manager		
Work Package Name			Work Package No.		Work Package Manager			Contact Info	Date
Start Date		End Date		Critical Path Y N		Predecessor Work Package(s)			Successor Work Package(s)
TASK									
No.	Name	Description			Time (day s)	Responsibility		Contact Info.	
Prepared by			Date		Approved by			Date	
								Sheet 1 of 1	

Lesson **Five**: Launch of software project

Summary of Lesson **5**

- Using tools, templates, and processes to launch a TPM project
- Recruiting the project team
- Conducting the project kick-off meeting
- Establishing team operating rules
- Managing scope changes
- Managing team communications
- Assigning resources
- Resource-leveling strategies
- Finalizing the project schedule
- Writing work packages

Lesson **Five**: Launch of software project

Assignment I of Lesson **Five**

- Each team should design and write the **Project Charter** based on the characteristics of your course project.
- The contents of **Project Charter** should be written according to the template on the textbook.
- The team leader should submit **Project Charter** of your team on canvas platform before **29th March, 2026**.

Lesson **Five**: Launch of software project

Assignment I of Lesson **Five**

■ Sample of **Project Charter**

TABLE 4-1 Project charter for the DNA-sequencing instrument completion project

Project Title: DNA-Sequencing Instrument Completion Project

Date of Authorization: February 1

Project Start Date: February 1

Projected Finish Date: November 1

Key Schedule Milestones:

- Complete first version of the software by June 1
- Complete production version of the software by November 1

Budget Information: The firm has allocated \$1.5 million for this project, and more funds are available if needed. The majority of costs for this project will be internal labor. All hardware will be outsourced.

Lesson Five: Launch of software project

Assignment I of Lesson Five

■ Sample of Project Charter

TABLE 4-1 Project charter for the DNA-sequencing instrument completion project (cont)

Project Manager: Nick Carson, (650) 949-0707, ncarson@dnaconsulting.com

Project Objectives: The DNA-sequencing instrument project has been underway for three years. It is a crucial project for our company. This is the first charter for the project, and the objective is to complete the first version of the software for the instrument in four months and a production version in nine months.

Main Project Success Criteria: The software must meet all written specifications, be thoroughly tested, and be completed on time. The CEO will formally approve the project with advice from other key stakeholders.

Approach:

- Hire a technical replacement for Nick Carson and a part-time assistant as soon as possible.
- Within one month, develop a clear work breakdown structure, scope statement, and Gantt chart detailing the work required to complete the DNA sequencing instrument.
- Purchase all required hardware upgrades within two months.
- Hold weekly progress review meetings with the core project team and the sponsor.
- Conduct thorough software testing per the approved test plans.

ROLES AND RESPONSIBILITIES

Name	Role	Position	Contact Information
Ahmed Abrams	Sponsor	CEO	aabrams@dnaconsulting.com
Nick Carson	Project Manager	Manager	ncarson@dnaconsulting.com
Susan Johnson	Team Member	DNA expert	sjohnson@dnaconsulting.com
Renyong Chi	Team Member	Testing expert	rchi@dnaconsulting.com
Erik Haus	Team Member	Programmer	ehaus@dnaconsulting.com
Bill Strom	Team Member	Programmer	bstrom@dnaconsulting.com
Maggie Elliot	Team Member	Programmer	melliot@dnaconsulting.com

Sign-off: (Signatures of all the above stakeholders)

Ahmed Abrams
Susan Johnson
Erik Haus
Maggie Elliot

Nick Carson
Renyong Chi
Bill Strom

Comments: (Handwritten or typed comments from above stakeholders, if applicable)

"I want to be heavily involved in this project. It is crucial to our company's success, and I expect everyone to help make it succeed." —Ahmed Abrams

"The software test plans are complete and well documented. If anyone has questions, do not hesitate to contact me." —Renyong Chi
